# **2018 Capital Project Progress Report**

- Project Scope
  - Window Replacements
  - Roof Replacements
  - HVAC Improvements
- Project Schedule
- Project Budget





# **District Wide Scope of Work**

### Phase 3.1 - 2019 Window Replacement

- John Jay HS
- Brinckerhoff ES
- Gayhead ES
- Kinry Road ES
- Myers Corners ES
- Sheafe Road ES

Phase 3.1 Roof Replacement

Fishkill Plains ES

### Phase 3.2 - 2020 and 2021 HVAC Improvements

- Roy C Ketcham HS
  Replace Boilers and Steam Heating System
- John Jay HS
  Replace Steam Heating System
- Myers Corners ES
  Replace Unit Ventilators



2018 Capital Project Progress Report Wappingers Central School District RHINEBECK ARCHITECTURE

### **Previous Window Replacement Work**

- R. C. Ketcham HS
- Van Wyck Junior HS
- Fishkill ES
- Fishkill Plains ES
- James Evans ES
- Oak Grove ES
- Vassar Road ES
- Wappingers Junior HS



Van Wyck Jr HS





Vassar Road ES



**2018 Capital Project Progress Report Wappingers Central School District** RHINEBECK ARCHITECTURE

### Window Replacement – John Jay High School - Existing








**Existing Windows** 



2018 Capital Project Progress Report Wappingers Central School District RHINEBECK ARCHITECTURE

### Window Replacement – John Jay High School

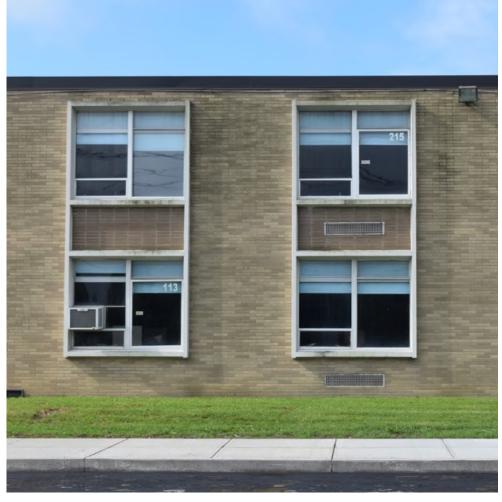

**Existing Windows** 



**New Windows** 



2018 Capital Project Progress Report Wappingers Central School District RHINEBECK ARCHITECTURE

### Window Replacement – Brinckerhoff and Gayhead Elementary Schools



**Existing Windows** 



New Windows (Similar to Fishkill Plains ES)



## Window Replacement – Brinckerhoff Elementary School

#### **Existing Cafeteria**







#### Similar to Oak Grove ES Cafeteria





**2018 Capital Project Progress Report Wappingers Central School District** RHINEBECK ARCHITECTURE

# Window Replacement – Kinry Road Elementary School



**Existing Windows** 

**New Windows** 



# Window Replacement – Myers Corners Elementary School



**Existing Windows** 

**New Windows** 



2018 Capital Project Progress Report Wappingers Central School District RHINEBECK ARCHITECTURE

# Window Replacement – Sheafe Road Elementary School



**Existing Windows** 



**New Windows** (Similar to Fishkill Plains ES)



**2018** Capital Project Progress Report **Wappingers Central School District** RHINEBECK ARCHITECTURE

# **Roof Replacement – Fishkill Plains Elementary School**



57,000 sf Roof on Tectum and Wood Plank Deck. Installed in 1990's

New roof system to provide 25 year warranty.



**2018 Capital Project Progress Report Wappingers Central School District** RHINEBECK ARCHITECTURE

### **Project Schedule – Phase 3.1**

Construction Documents October 2018
 SED Review Complete December 2018
 Bid & Award January 2019
 Construction Starts June 2019

#### **Project Schedule – Phase 3.2 - HVAC**

- **Construction Documents** October 2018 \*\* March 2019 \*\* Design Development Construction Documents June 2019 • \*\* Expedited SED Review September 2019 Bid & Award October 2019 \*\* **Construction Starts** June 2020 •
- Construction Complete September 2021






2018 Capital Project Progress Report Wappingers Central School District RHINEBECK ARCHITECTURE





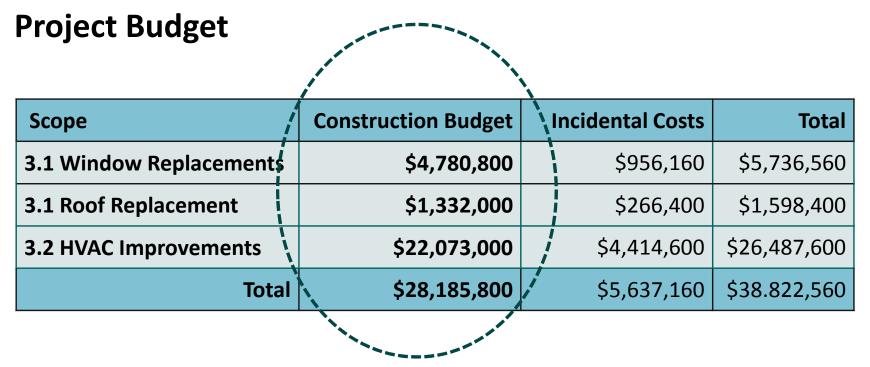

Cost Estimates will be prepared for Phase 3.1 in October 2018, and for Phase 3.2 at each Design Phase (October, March and June 2019)

